




		Jméno	Trvání	Začátek	Konec	...	J...	Čtvr 2, 2013					Čtvr 3, 2013			Čtvr 4, 2013			Čtvr 1, 2014			Čtvr 2, 2014			Čtvr 3, 2014			Čtvr 4, 2014			Čtvr 1, 2015			Čtvr 2, 2015									
								II	III	IV	V	VI	VII	VIII	IX	X	XI	XII	I	II	III	IV	V	VI	VII	VIII	IX	X	XI	XII	I	II	III	IV	V								
40		Demolition and excavation	26 dní	2.6.14...	7.7.14...																																						
41		Fondation, canalistaion and drainign	35 dní	2.6.14...	18.7.14...																																						
42		☐roof	40 dní	2.6.14...	25.7.14...																																						
43		checking of wooden structure, paint	25 dní	2.6.14...	4.7.14...																																						
44		New roof cladding and repair	30 dní	2.6.14...	11.7.14...																																						
45		Insulation and down ceiling	35 dní	9.6.14...	25.7.14...																																						
46		☐1.floor	92 dní	20.6.14...	27.10.1...																																						
47		Raw flooring	28 dní	20.6.14...	29.7.14...																																						
48		Cables and tubes	25 dní	21.7.14...	22.8.14...																																						
49		Windows	30 dní	28.7.14...	5.9.14...																																						
50		Doors	30 dní	14.8.14...	25.9.14...																																						
51		Plastering	25 dní	1.9.14...	3.10.14...																																						
52		Final floor	15 dní	25.9.14...	16.10.1...																																						
53		Painting and finishing surfaces	15 dní	3.10.14...	23.10.1...																																						
54		Finishing works	20 dní	30.9.14...	27.10.1...																																						
55		☐2.floor	97,8...	16.6.14...	29.10.1...																																						
56		Raw flooring	30 dní	16.6.14...	25.7.14...																																						
57		Cables and tubes	30 dní	30.6.14...	8.8.14...																																						
58		Windows	30 dní	14.7.14...	22.8.14...																																						
59		Doors	18 dní	5.8.14...	28.8.14...																																						
60		Plastering	21 dní	25.8.14...	22.9.14...																																						
61		Final floor	27 dní	8.9.14...	14.10.1...																																						
62		Painting and finishing	8 dní	6.10.14...	15.10.1...																																						
63		Finishing works	25 dní	24.9.14...	29.10.1...																																						
64		☐Technical rooms and equipment	78 dní	30.6.14...	15.10.1...																																						
65		Raw works	41 dní	30.6.14...	25.8.14...																																						
66		Technologie assembling	21 dní	4.8.14...	1.9.14...																																						
67		Connecting to nets	20 dní	15.8.14...	11.9.14...																																						
68		Connecting to electricity	22 dní	27.8.14...	25.9.14...																																						
69		Testing ang putting into operation	20 dní	18.9.14...	15.10.1...																																						
70		☐Staircase A	49 dní	7.7.14...	11.9.14...																																						
71		concrete structure	28 dní	7.7.14...	13.8.14...																																						
72		Interieur design	30 dní	11.7.14...	22.8.14...																																						
73		Finishing	14 dní	25.8.14...	11.9.14...																																						
74		☐Staircase B	42,6...	14.7.14...	10.9.14...																																						
75		concrete structure	35 dní	14.7.14...	29.8.14...																																						
76		Interieur design	26 dní	18.7.14...	25.8.14...																																						
77		Finishing	9 dní	28.8.14...	10.9.14...																																						
78		General cleaning	7 dní	19.9.14...	29.9.14...																																						
79		☐Connections	63 dní	21.7.14...	15.10.1...																																						
80		Sawage	41 dní	21.7.14...	15.9.14...																																						
81		Gas	27 dní	21.7.14...	26.8.14...																																						
82		Water	41 dní	21.7.14...	15.9.14...																																						

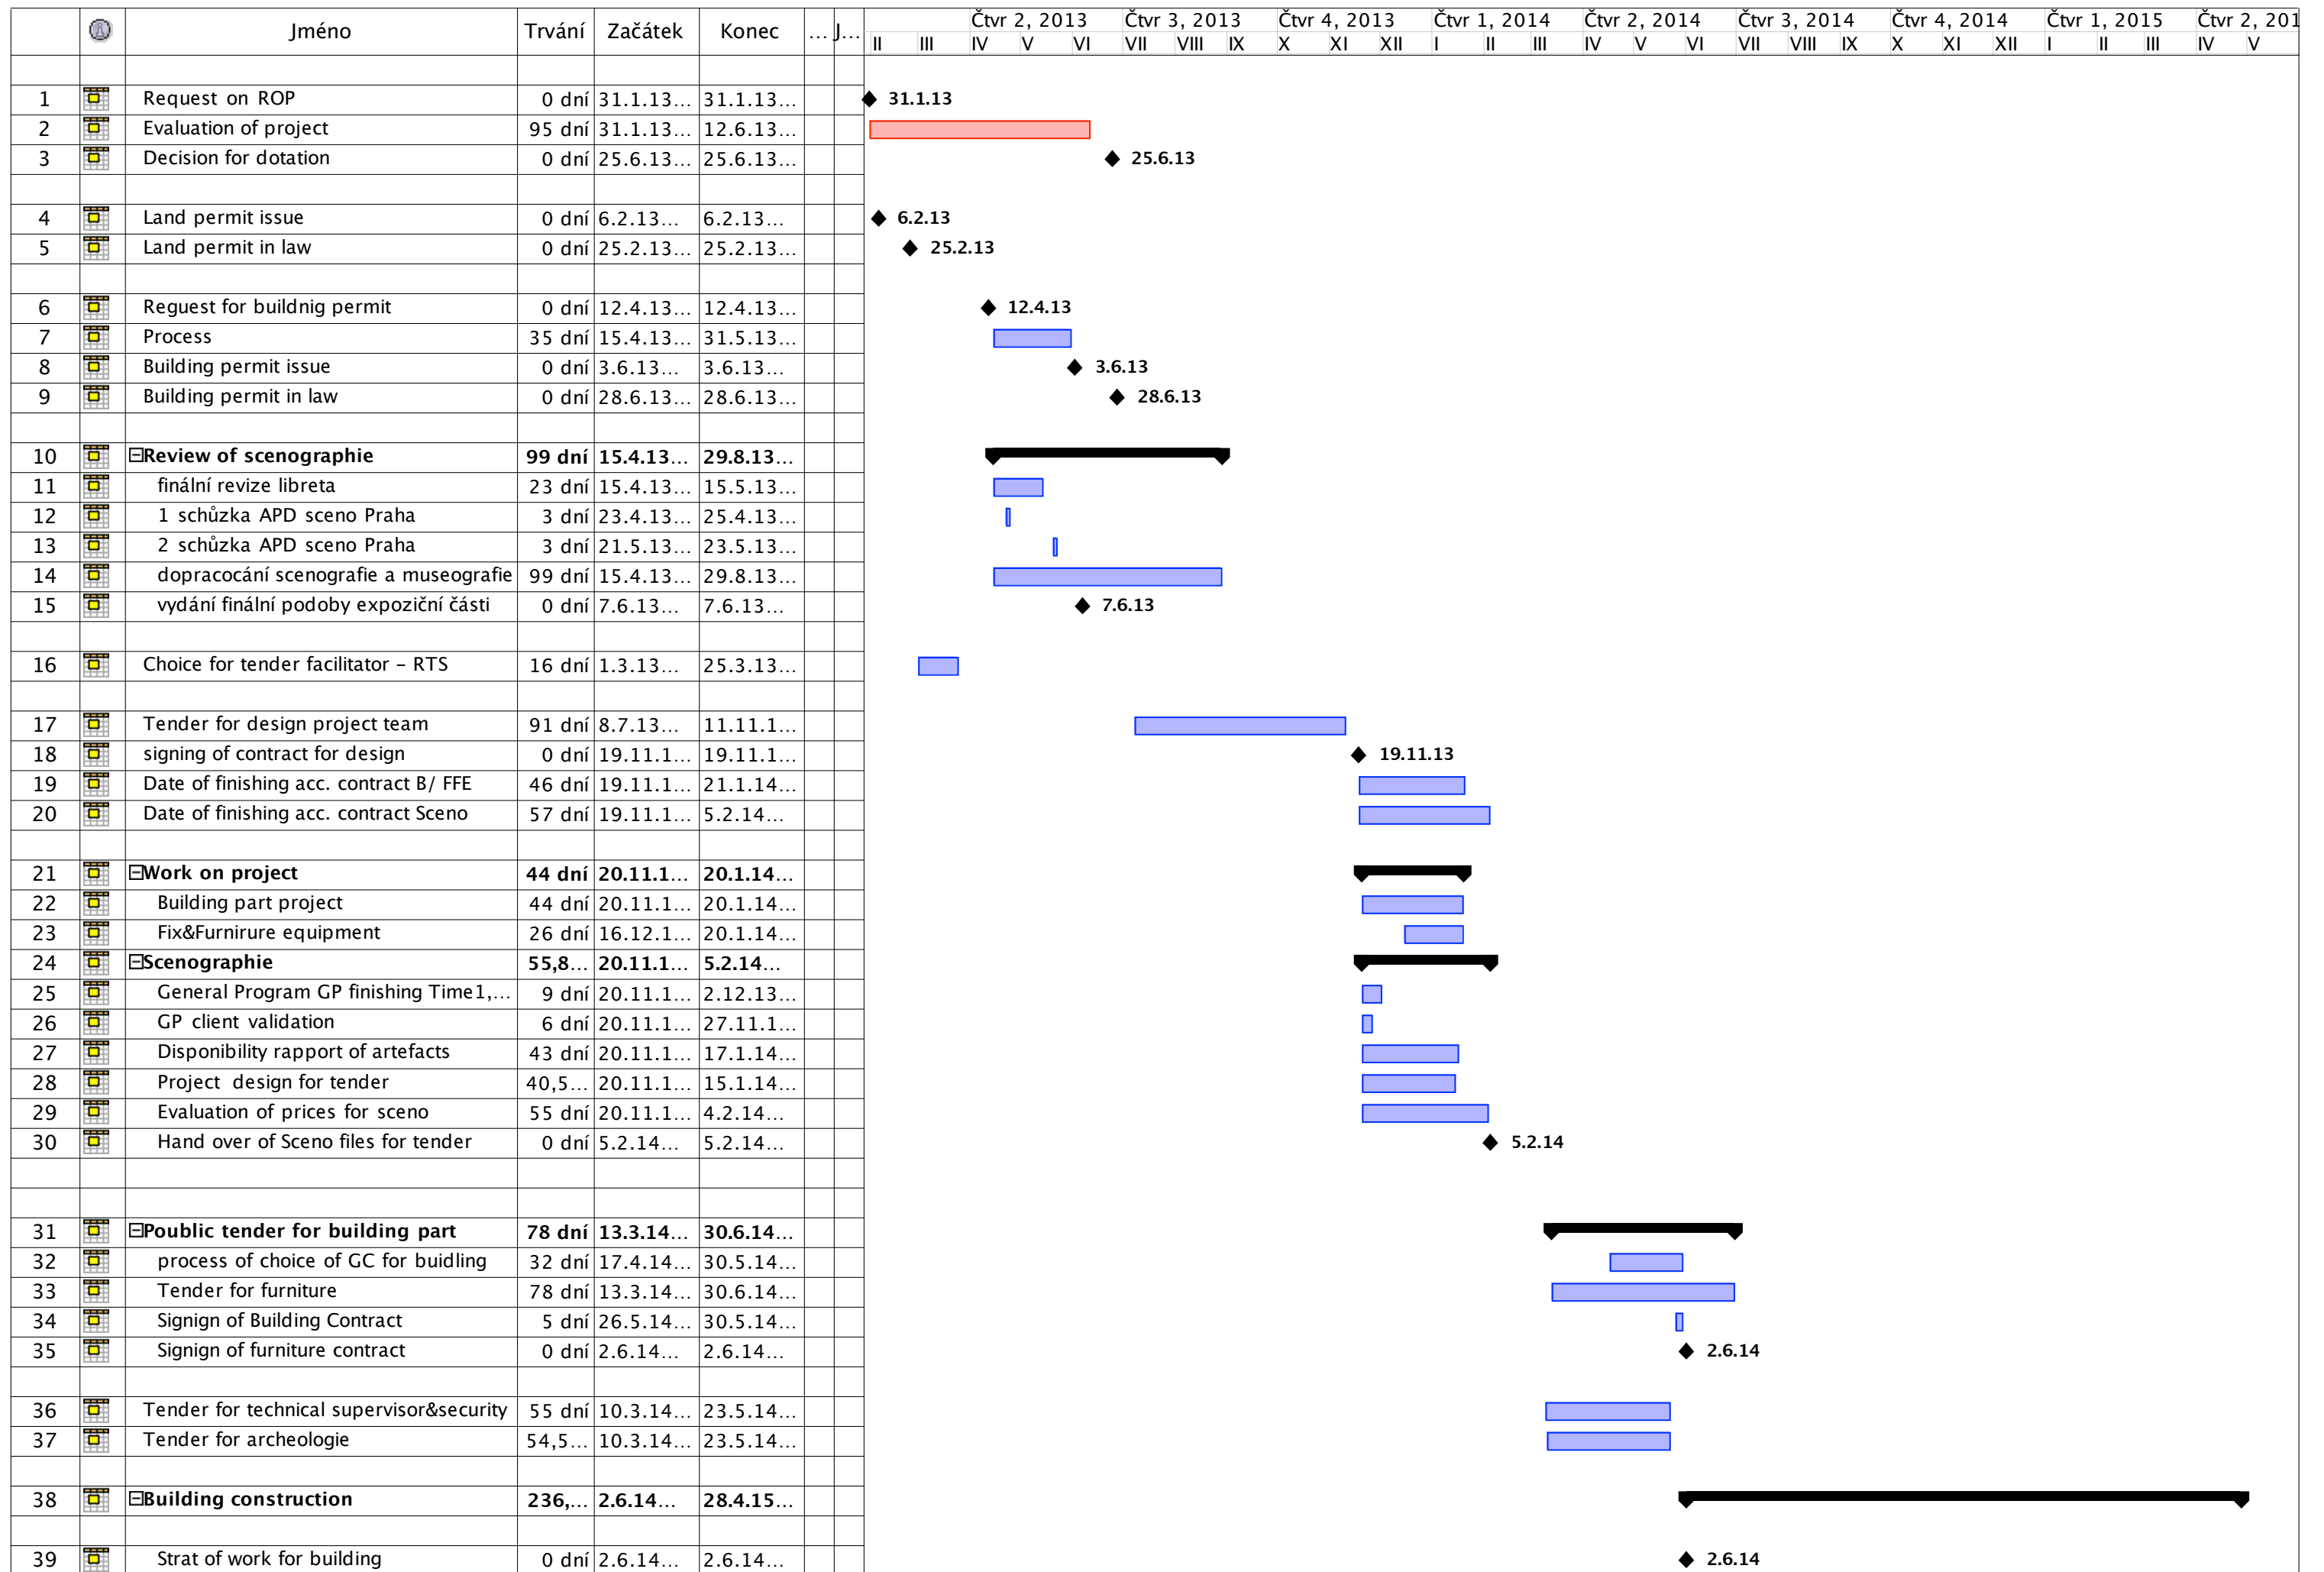
